

~~SECRET~~

EAPG 8-5589

COPY / OF /

CMCC Doc. No. 151X5.1020

Page 1 of 2Copy 1 of 2

March 11, 1958

Dear Dan:

Enclosed are the monthly delivery status reports and project fund status reports. The delivery status reports cover Systems 1, 3, 4 and Data Reduction Equipment as of March 2, 1958. The project fund status for Contracts A-101, A-102 and A-103 is shown as of January 31, 1958.

The last of the System 1 C5's and C6's continues to be delayed in order to complete special laboratory tests. We are holding the last System 3 test set to use in testing the balance of the receivers.

The System 4 schedule has been revised by the decision to environmentally test and flight test each complete system. This increased test program will require additional funds and a proposal is being prepared for this purpose.

Delivery of the final A, B1 and B2 racks and two C racks of Data Reduction Equipment continues to be delayed for lack of modified monitor and mixer chassis. The modifications can begin as soon as the monitors and mixers are obtained from the carrier. In addition, having only one C rack to use in testing A, B1, B2 and E racks has caused some delay. The recent cancellation, reinstatement and revised scope of work on the F racks has caused the schedule to be moved further ahead. Delay in the delivery of tape transports from the supplier has delayed delivery of G, H, J and K racks. The L rack schedule has been dropped due to a stop order. System 4 test requirements have caused the M rack schedule to be moved ahead. The delivery of the N rack has been delayed in order to modify the amplifier.

Although the cost report as of January 31, 1958, shows R&D costs incurred exceeded contract funds through Amendment No. 14, it should be recognized that we have submitted a number of cost estimates for which work has been authorized and which were not included in Amendment No. 14. We presume that Amendment No. 15 currently being prepared will take into account all authorized work and the related funding requirements.

Sincerely,


Sid

This document contains information affecting the national defense of the United States within the meaning of the Espionage Laws, Title 18 U.S.C., Section 793 and 794. Its transmission or the revelation of its contents in any manner to an unauthorized person is prohibited by law.

~~SECRET~~

SECRET

CMCC Doc. No. 151x5.1020

Page 2 of 2

Copy 1 of 2

Enclosures:

2 copies of each of the following:

Delivery Status Reports, Systems 1, 3 and
Data Reduction, Customers A, B and C

Delivery Status Reports, Systems 4 and 5,
Customer A

Delivery Status Reports, System 4, Customer
C

Project Fund Status A-101, A-102 and A-103

A-101 Cost Report

Copies 5a, 5b and 5c of following:

CMCC Doc. No. 221x5.11A

CMCC Doc. No. 221x5.3B

CMCC Doc. 221x5.7A

CMCC Doc. No. 221x5.4, Rev. 1

SECRET

TO: [REDACTED] 25X1 Approved For Release 2006/11/04 : CIA-RDP81B00878R000200030078-6

SUBJECT: Delivery Status Report System One, Customer "A"

REPORT PERIOD: February 11, 1958 to February 25, 1958

25X1

<u>ITEM</u>	<u>MP NUMBER</u>	<u>NOMENCLATURE</u>	<u>QUANTITY SHIPPED IN REPORT PERIOD</u>	<u>TOTAL QUANTITY AUTHORIZED</u>	<u>QUANTITY SCHEDULED FOR SHIPMENT DURING REPORT PERIOD</u>	<u>QUANTITY SHIPPED TO DATE</u>	<u>BALANCE DUE</u>
1.	10641	C ₁ Unit for S/1	0	74	0	74	0
2.	10406	C ₂ Unit for S/1	0	45	0	40	5(1)
3.	10737	B Unit for S/1	0	36	0	36	0
4.	10308	A ₂ Unit for S/1	0	34	0	34	0
5.	10922	A ₁ Unit for S/1	0	40	0	40	0
6.	63003	Cable Assembly Coaxial 0		46	0	46	0
7.	63004	Cable, C ₁ Unit and C ₂ Unit to Bulkhead	0	23	0	23	0
8.	63005	Cable, C ₁ Unit to C ₂ Unit	0	23	0	23	0
9.	10993	Cable Assembly (With Heater Plug)	0	23	0	23	0
10.	10566	D Unit - Test Set	1	8	1	8	0
11.	FAK	Equipment List E	0	3	0	3	0
12.	180-Day	Equipment List D	0	1	0	1	0
13.	SLOE	Equipment List F (For S/1 and S/3)	0	3	0	3	0
14.	10493	Manual of Operating Instructions for S/1	0	109	0	109	0
15.		Ampex Equipment	0	4	0	4	0

SUBJECT: Delivery Status Report, System One, Customer "A"

Page 2

ITEM	NP NUMBER	NOMENCLATURE	QUANTITY SHIPPED IN REPORT PERIOD	TOTAL QUANTITY AUTHORIZED	QUANTITY SCHEDULED FOR SHIPMENT DURING REPORT PERIOD	QUANTITY SHIPPED TO DATE	BALANCE DUE
16.	70641	C ₃ Unit	0	36	0	36	0
17.		C ₃ Modification Kit	0	66	0	66	0
18.	11713	C ₄ Unit	0	45	0	45	0
19.	11567	TWT Amplifier	0	6	0	6	0
20.	70034	Adapter, Waveguide H-P, X281-A, for use with Item 19.	0	12	0	12	0
21.	63041	Cable, Coax RG-142/U for use with Item 19.	0	12	0	12	0
22.	11737	Cable, Video, for use with Item 19.	0	12	0	12	0
23.	11303	Preliminary Instruction Guide for TWT Amplifier	0	12	0	12	0
24.	50% Spares	Spares for TWT Amplifier per Equipment List KK	0	3	0	3	0
25.	11719	A ₃ Unit	0	40	0	40	0
26.	11600	A ₅ Unit	0	12	0	12	0

(1) Retained for test and training.

TO: 25X1

Approved For Release 2006/11/04 : CIA-RDP81B00878R000200030078-6

SUBJECT: Delivery Status Report, System 3, Customer "A"

REPORT PERIOD: February 11, 1958 to February 25, 1958

25X1

FROM:

ITEM	MP NUMBER	NOMENCLATURE	QUANTITY SHIPPED IN REPORT PERIOD	TOTAL QUANTITY AUTHORIZED	QUANTITY SCHEDULED FOR SHIPMENT DURING REPORT PERIOD	QUANTITY SHIPPED TO DATE	BALANCE DUE
1.	10199 or 11048	Receiver Unit S/3 Receiver Unit M-1, S/3	0	14	0	14	0
2.	10667	J Box S/3	0	14	0	14 ⁽¹⁾	0
3.	10806	Cable, Power	0	15	0	15	0
4.	10196	Cable, Antenna	0	15	0	15	0
5.	10171	Cable, Assembly S/3	0	15	0	15	0
6.	10929	Cable, B Unit	0	15	0	15	0
7.	10867	Manual of Operating Instructions for S/3	0	25	0	25	0
8.	11007	Preflight Test Set, S/3	0	5	0	5	0
9.	NONE	Conversion Kit S/3A, Consisting of 3 each MP-10535, Board, Etched Assembly O4A or Conversion Kit S/3A, Consisting of 3 each MP-10968, Board, Etched Assembly O4A (M-1)	0	14	0	14	0
10.	FAK	Equipment List S	0	3	0	3 ⁽²⁾	0
11.	180-Day	Equipment List T	0	1	0	1 ⁽³⁾	0

(1) Nine each of this quantity are MP-11048, Receivers M-1.

(2) Three FAKs shipped complete less MP-55039, Diode.

(3) One Depot list shipped MP-55039, Diode.

25X1
TO: Approved For Release 2006/11/04 : CIA-RDP81B00878R000200030078-6
CC:

SUBJECT: Delivery Status Report, Systems 4 and 5, Customer "A"

REPORT PERIOD: February 11, 1958 to February 25, 1958

25X1
FROM:

<u>ITEM</u>	<u>MP NUMBER</u>	<u>NOMENCLATURE</u>	<u>QUANTITY SHIPPED IN REPORT PERIOD</u>	<u>TOTAL QUANTITY AUTHORIZED</u>	<u>QUANTITY SCHEDULED FOR SHIPMENT DURING REPORT PERIOD</u>	<u>QUANTITY SHIPPED TO DATE</u>	<u>BALANCE DUE</u>
1	NL	System 4	0	3	1	2	1
2	NL	Test Set, System 4	0	2	1	1 ⁽¹⁾	1
3	NL	System 5	0	1	0	1	0
4	NL	System 5, M-1	0	2	0	2	0
5	FAK	System 4, Equipment List AA	0	2	0	1 ⁽¹⁾	1
6	DEPOT	System 4, Equipment List BB	0	1	0	0	1
7	SLOE	System 4, Equipment List CC	0	2	0	1 ⁽¹⁾	1
8	FAK	System 5, Equipment List X	0	1	0	1	0
9	FAK	System 5, M-1, Equipment List DD	0	2	2	PARTIAL	2

(1) These items shipped in an interim configuration.

TO: [REDACTED] 25X1 Approved For Release 2006/11/04 : CIA-RDP81B00878R000200030078-6

SUBJECT: Delivery Status Report Data Reduction Equipment
Customer "A"

REPORT PERIOD: February 11, 1958 to February 25, 1958

ITEM	MP NUMBER	NOMENCLATURE	QUANTITY SHIPPED IN REPORT PERIOD	TOTAL QUANTITY AUTHORIZED	QUANTITY SCHEDULED FOR SHIPMENT DURING REPORT PERIOD	QUANTITY SHIPPED TO DATE	BALANCE DUE
1.	10939	"A" Rack, Play-back Equipment	0	4	0	4	0
2.	11892	Guide, Instruction, "A" Rack	0	15	0	15	0
3.	10945	Manual, Operation & Maintenance, Ampex Tape Transport, Ampex Catalog No. 5700 (modified)	0	55	0	55	0
4.	10927	"B-1" Rack, Duplicating Equipment	0	4	0	4	0
5.	10948	"B-2" Rack, Duplicating Equipment	0	4	0	4	0
6.	10738	Guide, Instruction (for "B-1" & "B-2" Racks)	0	15	0	15	0
7.	10942	"C" Rack Playback Analysis Equipment	0	4	0	4	0
8.	10774	Guide, Instruction, "C" Rack	0	25	0	25	0
9.	10933	"F" Rack, Event Marker Equipment	0	6	0	5(1)	1
10.	10910	Guide, Instruction, "F" Rack	0	40	0	40	0

(1) Serial No. 1, 2, 3, 5 and 6 returned for rework and modification.

SUBJECT: Delivery Status Report Data Reduction Equipment,
Customer "A"

-2-

ITEM	MP NUMBER	NOMENCLATURE	QUANTITY SHIPPED IN REPORT PERIOD	TOTAL QUANTITY AUTHORIZED	QUANTITY SCHEDULED FOR SHIPMENT DURING REPORT PERIOD	QUANTITY SHIPPED TO DATE	BALANCE DUE
11.	10664	Guide, Instruction, Ampex Model 7784 - 4 Tape Transport	0	15	0	15	0
12.	10807	Data Reduction System Manual	0	25	0	0	25
13.	10549	"E" Rack	1	4	1	2	2
14.	10827	Guide Instruction, "E" Rack	0	25	0	25	0
15.		Modification Kit for "C" Rack	0	4			
16.		Modification Kit for "F" Rack	0	3			
17.		Modification Kit for Ampex Tape Transport	0	12	0	12	0
18.		Patch Cables for "A" Rack	0	4	1	3	1
19.		Patch Cables for "B-2" Rack	0	4	1	3	1
20.		Patch Cables for "C" Rack	0	4	1	3	1
21.		Patch Cables for "F" Rack	0	6	2	3	3
ACCOMPLISHED IN PRODUCTION OF UNITS							
ACCOMPLISHED IN PRODUCTION OF UNITS							

(2) Serial No. 1 returned for rework and modification.


SUBJECT: Delivery Status Report Data Reduction Equipment,
Customer "A"

-3-

ITEM	MP NUMBER	NOMENCLATURE	QUANTITY SHIPPED IN REPORT PERIOD	TOTAL QUANTITY AUTHORIZED	QUANTITY SCHEDULED FOR SHIPMENT DURING REPORT PERIOD	QUANTITY SHIPPED TO DATE	BALANCE DUE
22.	Equipment List Y-A	Fly Away Kit for "A" Rack	0	4	0	4(3)	0
23.	Equipment List Y-B	Fly Away Kit for "B-1" and "B-2" Racks	0	4	0	4(3)	0
24.	Equipment List Y-C	Fly Away Kit for "C" Rack	0	4	0	4(3)	0
25.	Equipment List Y-E	Fly Away Kit for "E" Rack	0	4	0	4(3)	0
26.	Equipment List Y-F	Fly Away Kit for "F" Rack	0	6	1	5(3)	1
27.	Equipment List Y	Depot Spares	0	1	0	0	1
28.	11085	"G" Rack	0	4	0	4	0
29.	11099	"H" Rack	0	3	2	3	0
30.	11022	"J" Rack	0	4	0	4	0
31.	11692	"K" Rack	0	3	2	3	0
32.	11388	"L" Rack	0	3	0	1	2
33.	11978	"M" Rack	0	4	0	2	2
34.	11550	"N" Rack	0	3	0	1	2

(3) These lists shipped less a few minor shortages.

Project A101 Fund Status

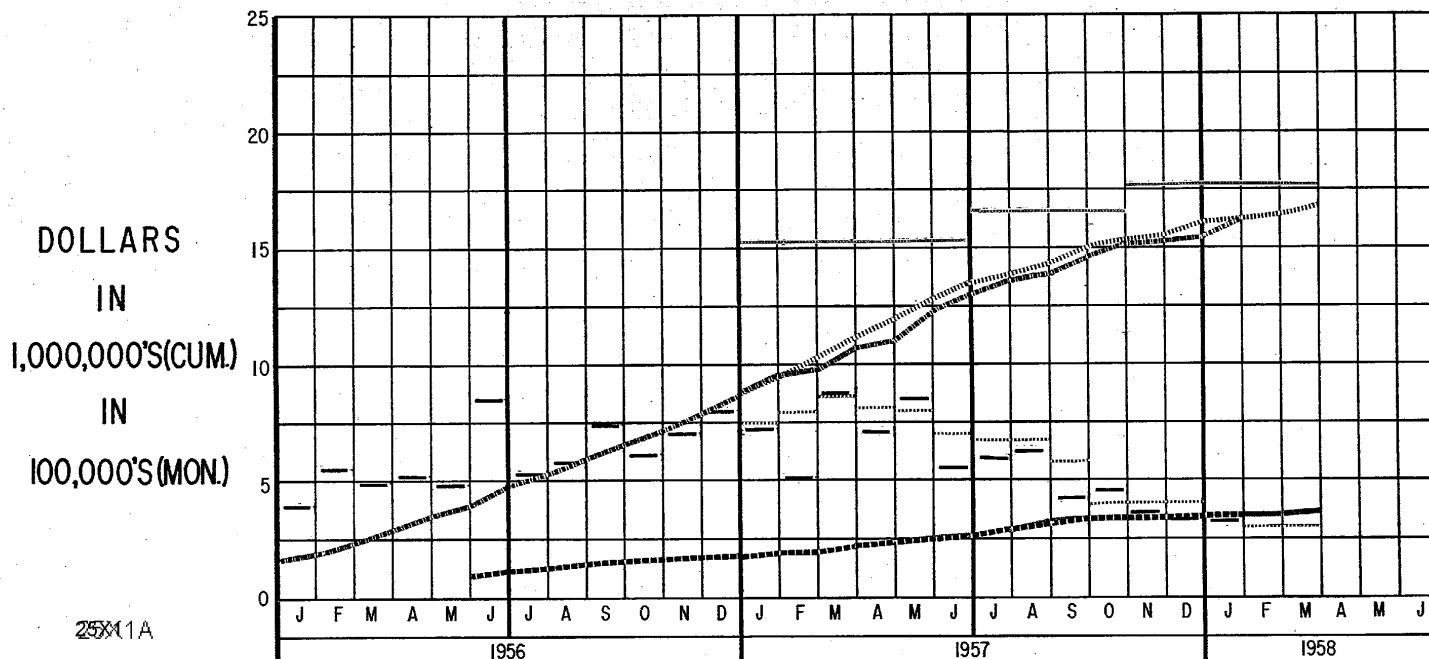

LABOR	FRCT
	ACTUA
OVERHEAD	FRCT
	ACTUA
MATERIAL	FRCT
	ACTUA
G & A	FRCT
	ACTUA
OTHER	FRCT
	ACTUA
TOTAL	FRCT
IN 100,000'S	ACTUA
MONTHLY	FRCT
IN 10,000'S	ACTUA

FORM NO. 1-57-000-000

DOLLARS
100,000'S(cum)
10,000'S(mon)

25X11 A

LABOR	FRCT
	ACTUAL
OVERHEAD	FRCT
	ACTUAL
OTHER DIRECT COSTS	FRCT
	ACTUAL
G & A	FRCT
	ACTUAL
OTHER	FRCT
	ACTUAL
TOTAL	FRCT
1,000's	ACTUAL
MONTHLY	FRCT
	ACTUAL




Project A-103 Fund Status

MJO 5040

DOLLARS
IN
100,000'S (CUM.)
IN
10,000'S (MON)

25X11A

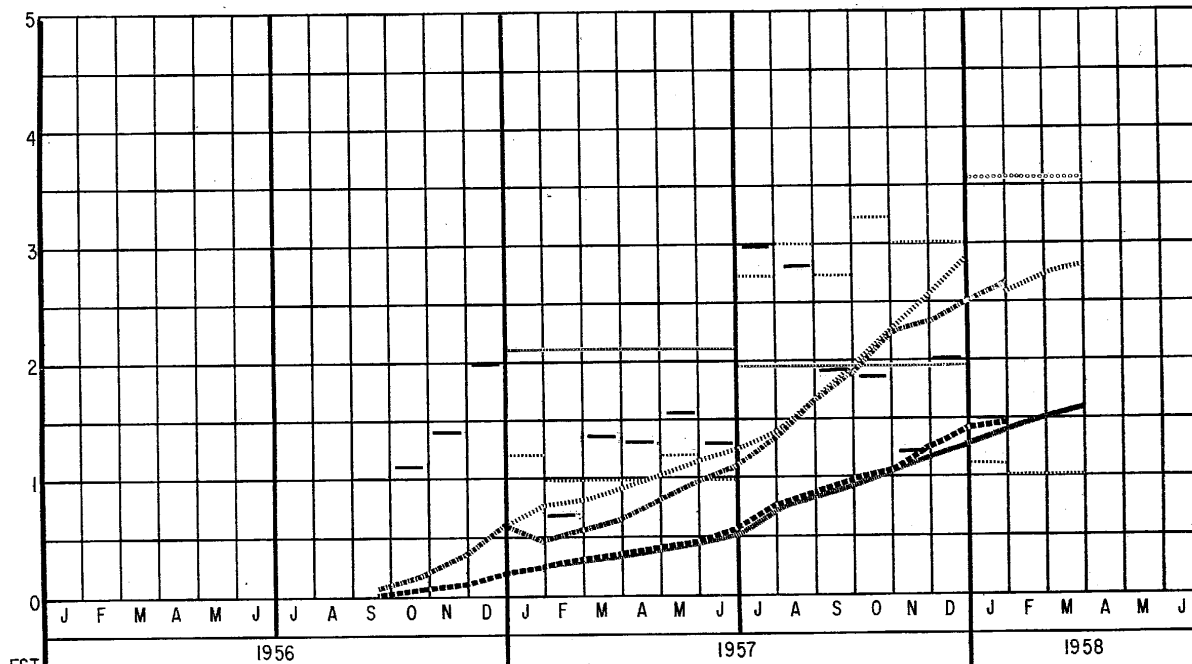

LABOR	PRGST
	ACTUAL
OVERHEAD	PRGST
	ACTUAL
MATERIAL	PRGST
	ACTUAL
G & A	PRGST
	ACTUAL
OTHER	PRGST
	ACTUAL
TOTAL	PRGST
IN 1,000'S	ACTUAL
MONTHLY	PRGST
	ACTUAL

25X1

Approved For Release 2006/11/04 : CIA-RDP81B00878R000200030078-6

Page Denied

Next 4 Page(s) In Document Denied

25X1

Approved For Release 2006/11/04 : CIA-RDP81B00878R000200030078-6
